

SONOS · GSEC

Olympia HWV

Kickoff Meeting



DATE

18 May 2026



PARTNERS

Sonos × GSEC



LOCATION

Online

AGENDA

Today's Discussion

Six sections, one shared goal — a smooth HWV kickoff for Olympia.

01



Welcome & Team

HWV leads · Product outlook

p. 3–6

02



HWV Requirements

SOW · Assessment · 4M · Scorecard

p. 7–13

03



Product Challenges

NuDD · AE · EE · ME changes

p. 14–45

04



Project Schedule & P1A Plan

P1A build plan · Master timeline

p. 46–50

05



Verification Scope

PKG · ME · ENV · CMF · EE · DMT

p. 51–53

06



Documentation

Confluence · Sonos BOX

p. 54–55

Sonos HWV Lead

Your points of contact for this program



SONOS HWV Lead

Toni Zhang



toni.zhang@sonos.com

- *PIE lead is responsible for Sonos product hardware/system design quality*
- *HWV management (schedule/progress/result review)*
- *Jira management (Filter Jira priority/Critical Jira debug)*
- *DOE management (DOE plan/DOE review/Critical issue FACA)*

BASED IN

Shanghai

China



31.23° N · 121.47° E

Pacific Standard / GMT+8

Product Outlook

Olympia — The best Sonos speaker yet

PROGRAM

Olympia

2

CMF variants


CMF COLORS



Sonos Black



Cloud White

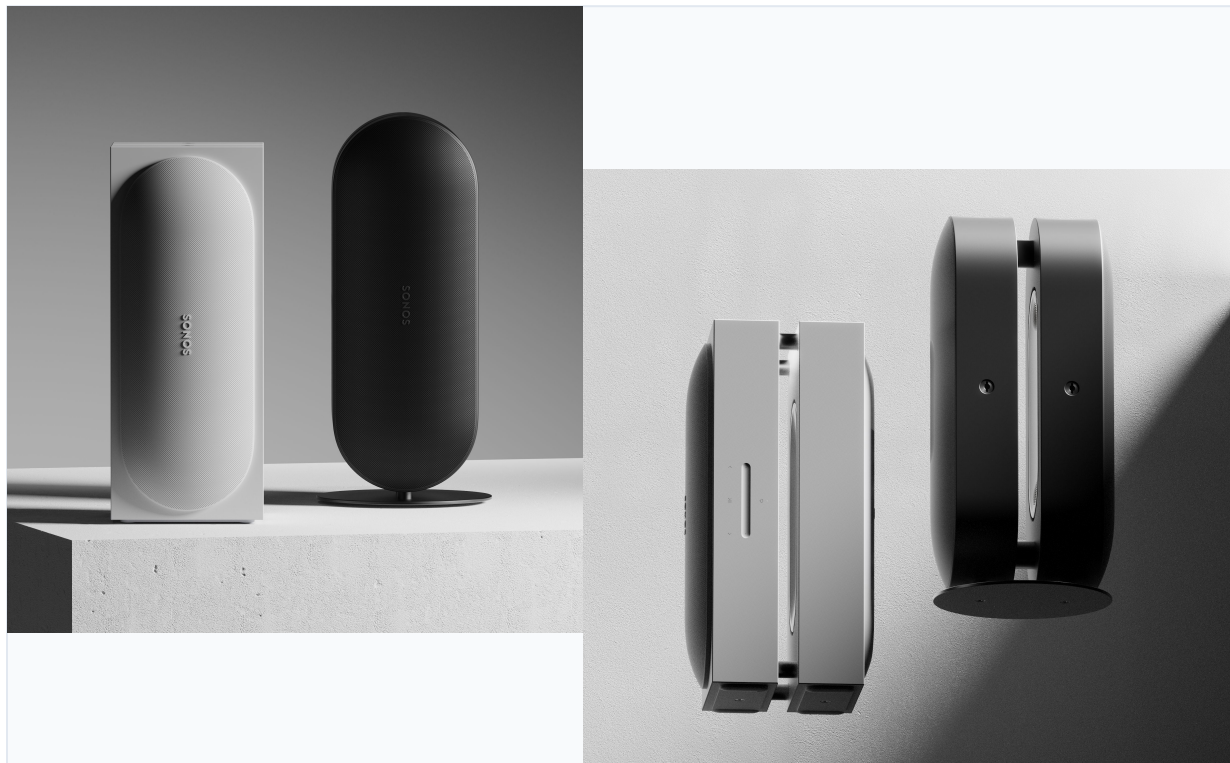


Product Outlook

Olympia — The best Sonos speaker yet

PROGRAM

Olympia

Hoagie is the most feasible to implement with higher wireless performance.

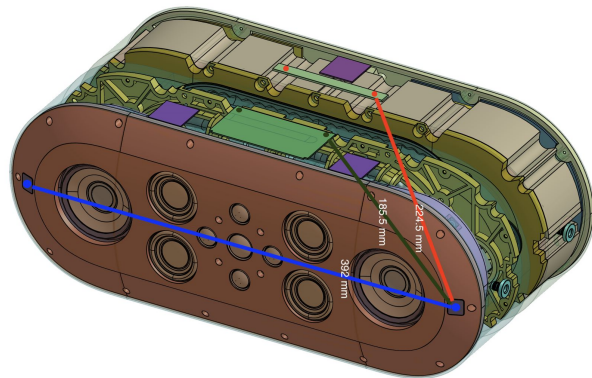

Product Outlook


Olympia — The best Sonos speaker yet

PROGRAM

Olympia

What's the challenge from 3D explosion?

- *GGEC's questions?*

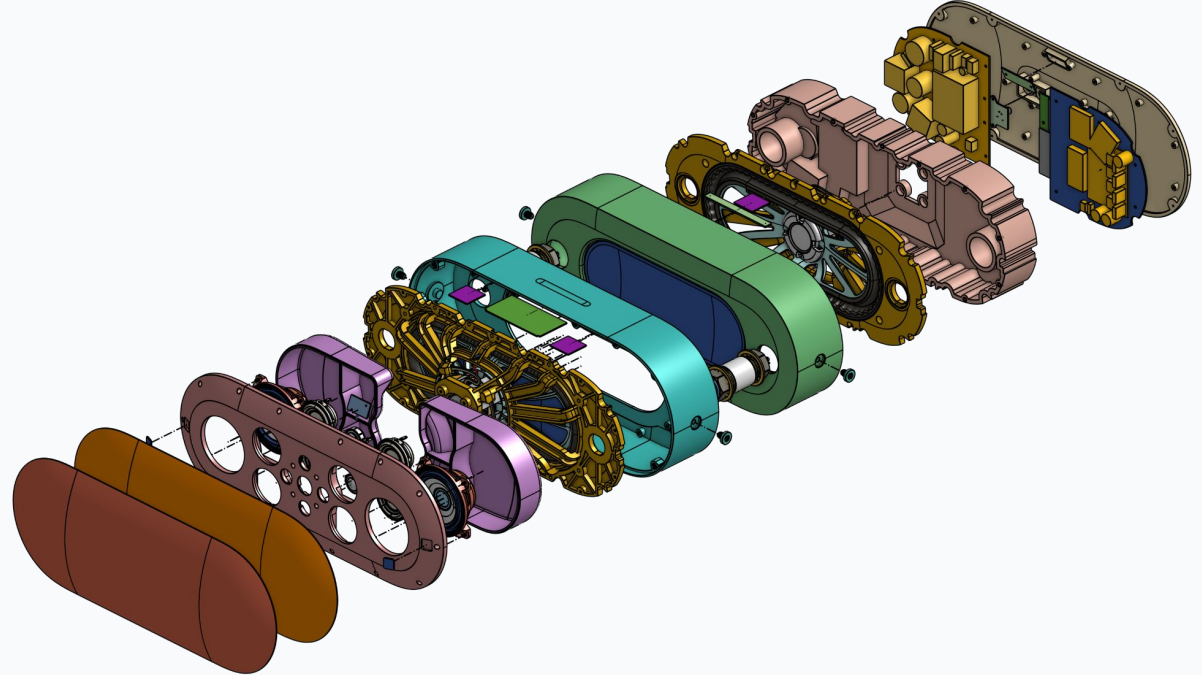

HWV Requirements

Scope, Capability, and Performance Framework for JDM & CM Partners

SOW — Scope

Assessment — Capability

4M — Readiness

Scorecard — Performance

General Requirements

SOW · Assessment · Scorecard — applies to all JDM & CM partners

SCOPE & R&R

Statement of Work

- HWV Development (Strategy)
- HWV Activities — Plan / Execute / Report
- Jira Bug & Failure Analysis
- Communication & Documentation
- NuDD exploration and test development

Manufacturer drives execution · Sonos drives strategy & approval

CAPABILITY CHECK

Assessment

- Sec 0: HWV Development Capability (JDM only)
- Sec 1: Engineering Capability
- Sec 2: Management & Process
- Sec 3: Documentation & Tools
- Sec 4–5: Resources, Equipment & Facility

Must be completed before interview / project start

PERFORMANCE MEASURE

Scorecard — 100 pts

- Communication — 10 pts
- Readiness — 20 pts
- Execution — 20 pts
- Schedule — 15 pts
- Report — 12 pts
- Post Review — 20 pts
- Infrastructure & Logistics — 3 pts

 JDM/CM must submit scorecard to Sonos for review at end of each HWV stage

The Framework

Four artifacts together define HWV Requirements



SCOPE • R&R

Statement of Work

Defines the boundary line — what the Manufacturer owns vs. what Sonos owns.

4 workstreams

- HWV Development (Strategy)
- HWV Activities (Plan/Execute/Report)
- Jira Bug & Failure Analysis
- Communication & Documentation



CAPABILITY CHECK

Assessment

Evaluates JDM/CM readiness before engagement and at each new project.

7 sections

- Development Capability (JDM)
- Engineering Capability
- Management & Process
- Docs, Tools, Resources, Facility



TESTING READINESS

4M Readiness

Confirms the project is ready to run — people, kit, consumables, and procedures.

4 categories

- Man — engineers & test staff
- Machine — chambers & equipment
- Material — samples & consumables
- Method — plans, SOPs, FA flow



PERFORMANCE

Scorecard

Tracks Timing + Quality across every build — weighted to 100 points.

100-pt measure

- Communication · Readiness
- Execution · Schedule
- Report · Post-review
- Infrastructure & Logistics

Statement of Work — Responsibility Split

Manufacturer drives execution; Sonos drives strategy and approval

Workstream



Manufacturer



Sonos



HWV Development (Strategy)

Propose HWV for NUDDs · Feedback on strategy, procedures, scripts · PIE equipment in place · Trained SOPs across sites

Provide high-level expectations · Drive & finalize strategy · Create/review Master Plan · Approve PFS, templates, SOPs



HWV Activities (Plan · Execute · Report)

Develop detailed plans · Execute in-house, coordinate external labs · Report status, findings, results accurately and on time

Provide guidelines, templates, best practices · Drive readiness/delivery criteria · Review progress and approve deliveries



Jira Bug & Failure Analysis

Identify & report issues promptly · Co-drive JIRA bugs, activate & maintain dashboard, tech-lead assignment & validate, ontime update, opening rate $\geq 80\%$, reporting ≤ 24 hrs & pre-meeting rules · FACA for JDM-owned areas · Propose FACA elsewhere · Assess downstream impact

Co-host JIRA meetings · Drive cross-functional resolution · Monitor timely closure · Provide guidance on JIRA usage



Communication & Documentation

Secure UUT / data handling · Shared tools (Slack, JIRA, Confluence, ~~TestRail~~, G-Drive, Box) · English docs · Organized in Sonos cloud

Provide comm and documentation guidelines · Review and approve critical docs and reports for quality

Assessment — 7-Section Capability Check

Section 0 is JDM-only; Sections 1–6 apply to both JDM and CM

0

HWV Development Capability

JDM ONLY

Dedicated HWV team · Lead expertise · Strategy coverage & quality · Engineer capabilities (thermal, DMT, FW)

1

Engineering Capability

Communication · 4M1E readiness · Execution (Group A–D) · Post-check (visual, tear-down, FA)

2

Management & Process

Backup · R&R · Escalation · Risk · Bug management · FACA · Samples · Training · Long-term plan

3

Documentation & Tools

Slack / G-Drive / TestRail / JIRA · Templates · Daily & official reports · Database · Scorecard

4

Resources & Escalation

Capable team roster · Leader commitment · Clear escalation channels

5

Equipment & Facility

Current capability vs. HWV Equipment template · Gap list · Action plan to close

6

Open Topics

CM / JDM shares items worthy of Sonos attention — value-added insights welcome

4M Readiness

Man · Machine · Material · Method — required before HWV commence



Man

- Engineers & direct labor familiar with PKG, ME, ENV, CMF
- CPU SI and power test engineer
- Thermal test engineer
- Audio test engineer
- Linux OS familiarity
- SW engineer for HWV test scripts



Machine

- Climatic chamber
- ISTA-3A test environment
- ME-related test machines & equipment
- CMF-related test machines & chambers
- Group D EE test equipment (incl. thermal)
- Group C eDMT test equipment



Material

- CMF3 test chemicals
- CMF test consumables
- CMF piece-part samples (qty per project)



Method

- Group A, B, C, D test plans & procedures
- Test setups for ENV operational, EDMT, thermal...
- Readiness tracking list
- Tear-down SOP
- Tear-down checklist
- Post-FA flow

Scorecard — 100-Point Performance Measure

Each criterion evaluated on Timing and Quality

WEIGHT BREAKDOWN (of 100)

20

Readiness

Team roster · Equipment · Internal align · Test development

20

Execution

Stressing · Post-check · Supportability · Failure investigation · DOE

20

Post review & improvement

Result review · Lesson-learn · Improvement actions

15

Schedule

Work planned · Plans delivered · Milestones met

12

Report

Daily · Test integration · Investigation · Official · Tracking

10

Communication

Email within 1 working day · Proactive calls · Positive conduct

3

Infrastructure & logistics

Facilities · IT · Transportation

SCORED ON

T

Timing

On-time delivery of work product



Q

Quality

Accuracy & completeness of output

WHEN

- Weekly meeting · before build
- Dry run · before execution
- Daily whiteboard & report
- Post-build review · per stage

Product Challenges

What's changing on Olympia — NuDD & Risk list, AE, EE and ME updates



NuDD Risk List



AE Challenge



ME Challenge



EE Challenge

NuDD & Risk List

All below items are based on ACR and Olympia Incubation Qs/NUDDs/PKRs


CATEGORY	WORKSTREAM	Risk
AE	Gemini	High
	Multi Element Array	Middle
	Gemini Woofer Integration	High
ME	Foot - Multiple orientations	Middle
	Antenna- Multiple orientations	Low
	Microphone - Multiple orientations	Low
	Post - Material & Inside signal routing	Low
	Thermal	High
EE	Gemini AMP - MPS or Diodes	Middle
	Gemini woofer closed loop control	High
	HiFi 44.1KHz/88.2KHz	Low
	USB Line-in & RCA	Low
	2W idle power budget VS TTM tradeoffs	Middle
	EMC Risks	High

AE Challenge - Gemini

High efficiency, Low mass, Small space

What is Gemini?

- *Negative -K*
- It's an **assistive force**
- Examples in daily life


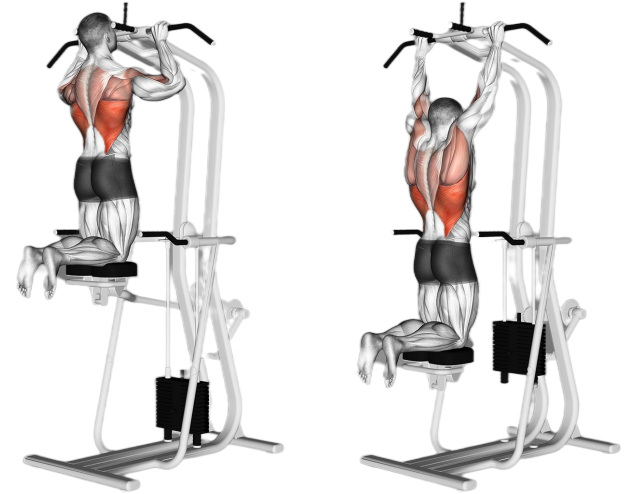


AE Challenge - Gemini



High efficiency, Low mass, Small space

Why do we need Gemini - Conventional VS Gemini



Woofer Free air

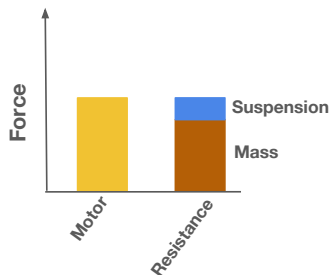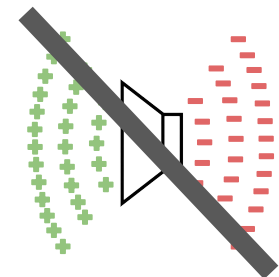



Sealed box

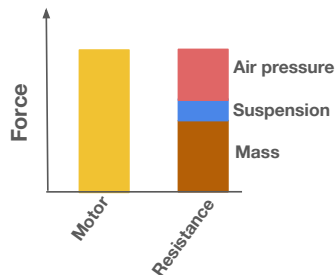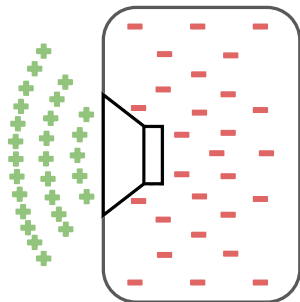

Small Sealed box

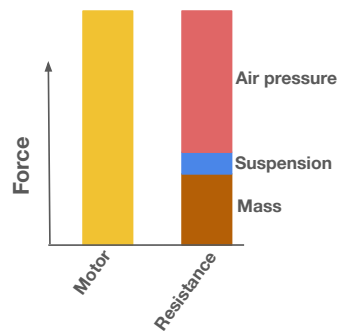

Small Sealed box + Gemini

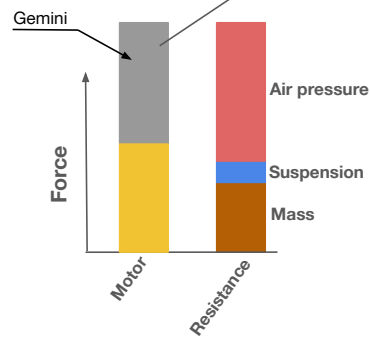


Power efficiency gain

**Realized efficiency gain is frequency/Impedance dependent.

AE Challenge - Gemini

High efficiency, Low mass, Small space


How do we create Gemini

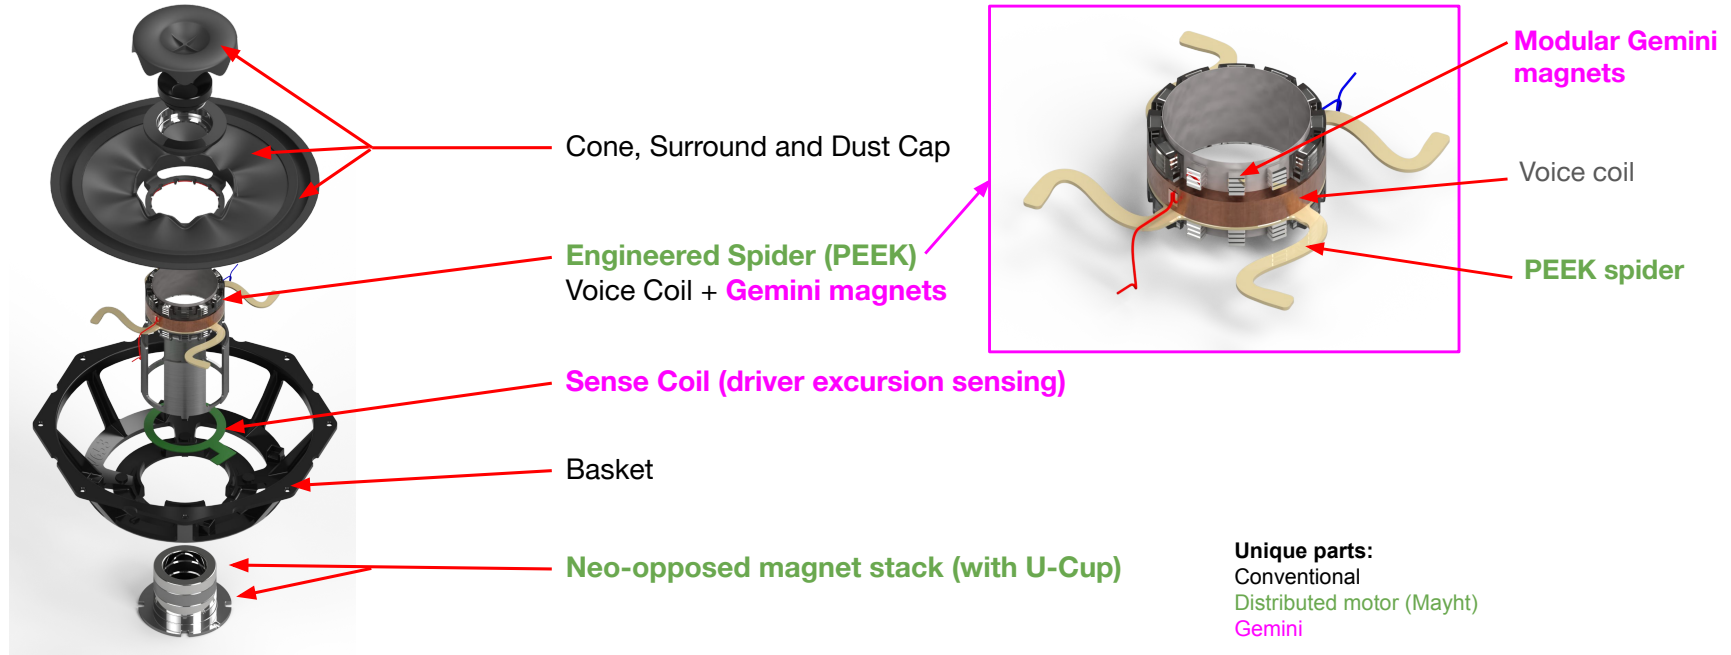

AE Challenge - Gemini

High efficiency, Low mass, Small space

How does Gemini move


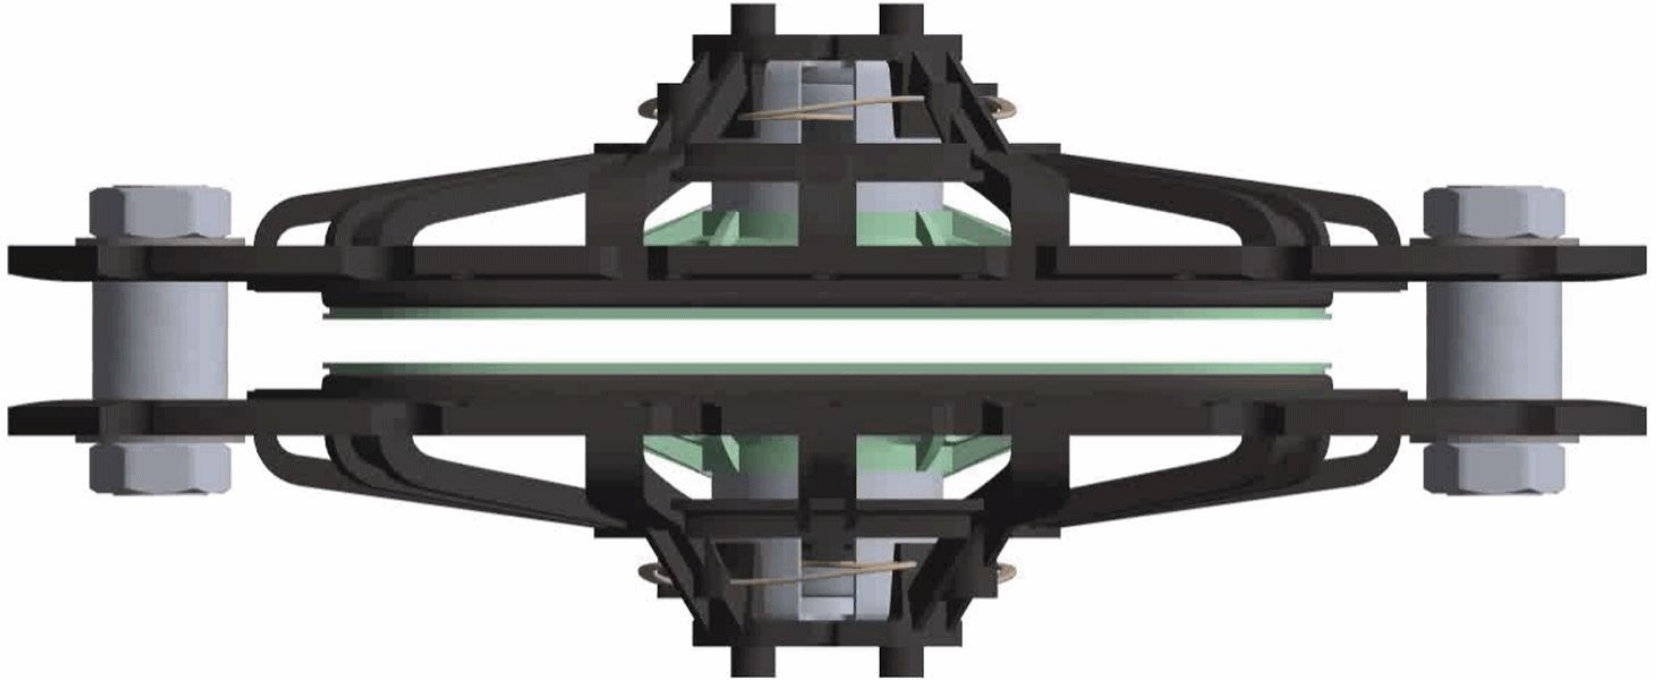


AE Challenge - Gemini

High efficiency, Low mass, Small space

What does HWV care about - MBB VS Gemini

- *Some experiences from MBB (similar design)*
 - *Cone broken*
 - *Spider broken*
 - *Ribe detached*

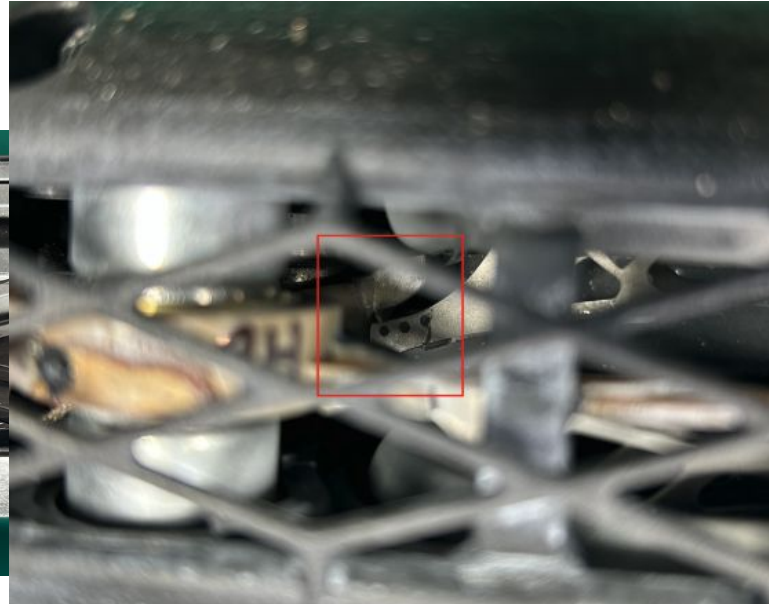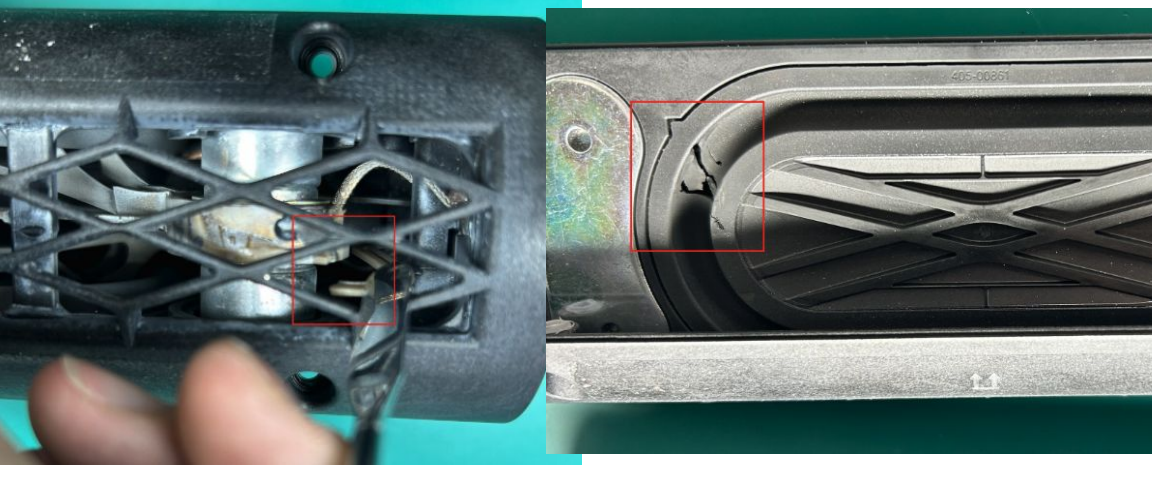

AE Challenge - Gemini

High efficiency, Low mass, Small space

How can HWV find issue - Gemini

- *Gemini should PASS component level TE tests*
- *System level ADMT test (1000 hours) from P2A*
 - *Air leak check and data record before and after stressing - GGEC why?*
 - *Check FA air leak while interval check failed*
 - *Interval check fixed process and pending check*
 - *Interval time = 100 hours*
 - *Conventional required post FA check: SPL / Sweeping 2*
 - *Pending special required check: Manual listening with diag wav file*

AE Challenge - Gemini woofer integration

High efficiency, Low mass, Small space

How do we integrate - Gemini


Gemini Transducer



DC capable amplifier



Control System




- *Why does Gemini need DC pulse - GGEC*

AE/EE Challenge - Gemini woofer integration

High efficiency, Low mass, Small space


Traditional Woofer Amplifier

- Class H improves efficiency and lowers idle losses
- ZCM used in Pallas further improves efficiency

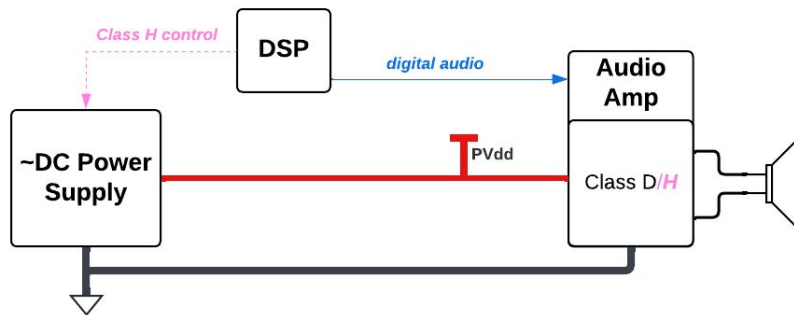

Gemini Woofer Amplifier

- Requires a DC pulse for 'liftoff', ~384 joules per woofer
- Requires additional feedback signals to control voice coil position and maintain stability
- Requires OCP HW protection circuit for product safety

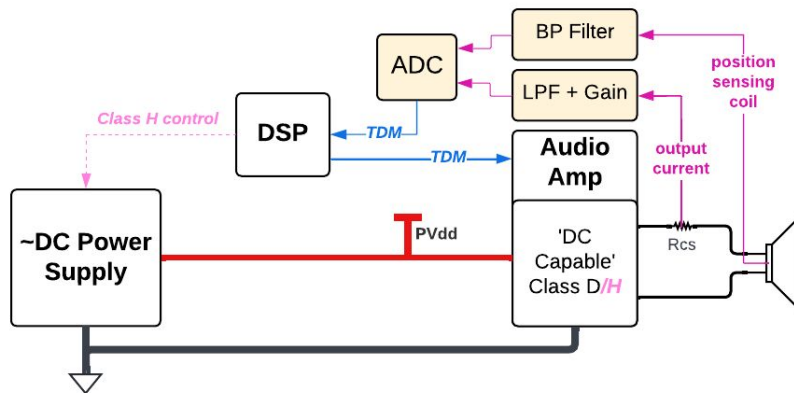

AE Challenge - Gemini woofer integration

High efficiency, Low mass, Small space

What does HWV care about - Gemini system


- *DC power for liftoff*
 - *Idle state VS OFF state*
- *Gemini control system*
 - *DSP algorithm verification*
 - *Stability under temperature changes*
 - *Stability under altitude changes (max 3000m) - GGEC check altitude chamber capacity*
- *OCP function*
 - *How to test?*

AE Challenge - Gemini woofer integration


High efficiency, Low mass, Small space

What does HWV care about Gemini - Altitude Test


Small Sealed box + Gemini +
high altitude

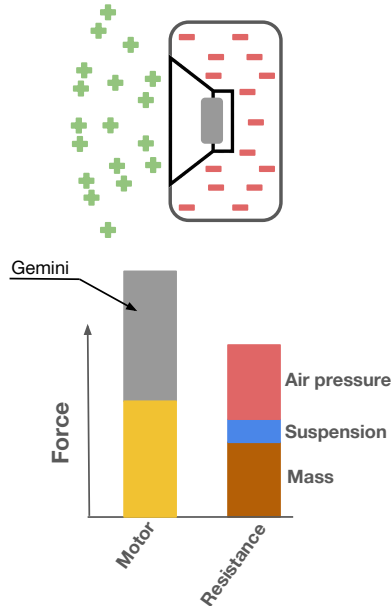

Variable Sealed box +
Gemini + high altitude

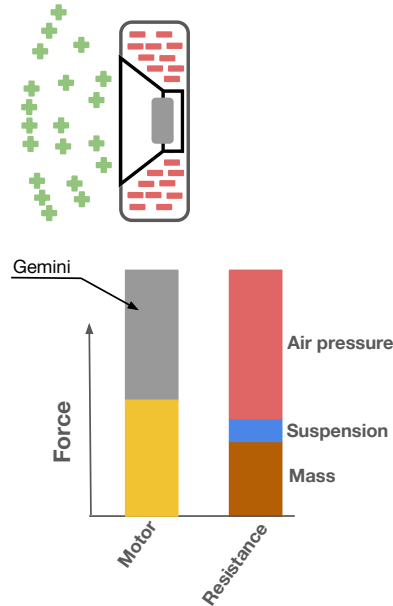

Small Sealed box + **Variable**
Gemini + high altitude

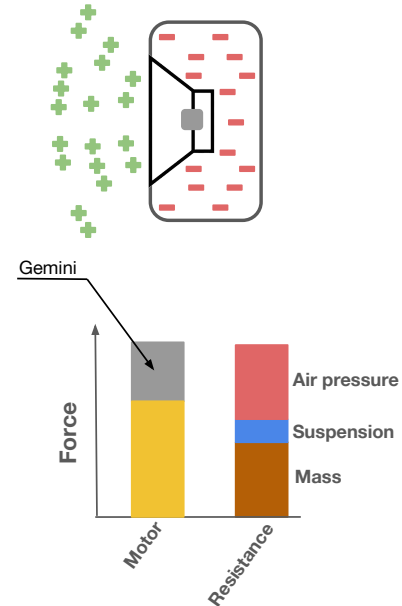

AE Challenge - Multi Element Array

Stereo Imaging, beam steering

What is Array?

Olympia is a four-way system, including the Gemini woofers.

The midbass transducers need to be custom, as nothing in the current Sonos portfolio is feasible from a size perspective or viable from a cost perspective.

The other transducers required are the:


- Center tweeter, one pcs.
- Arraying tweeter, two or four pcs.
- Mid range four pcs.



AE Challenge - Multi Element Array

Stereo Imaging, beam steering


What are the difficulties?

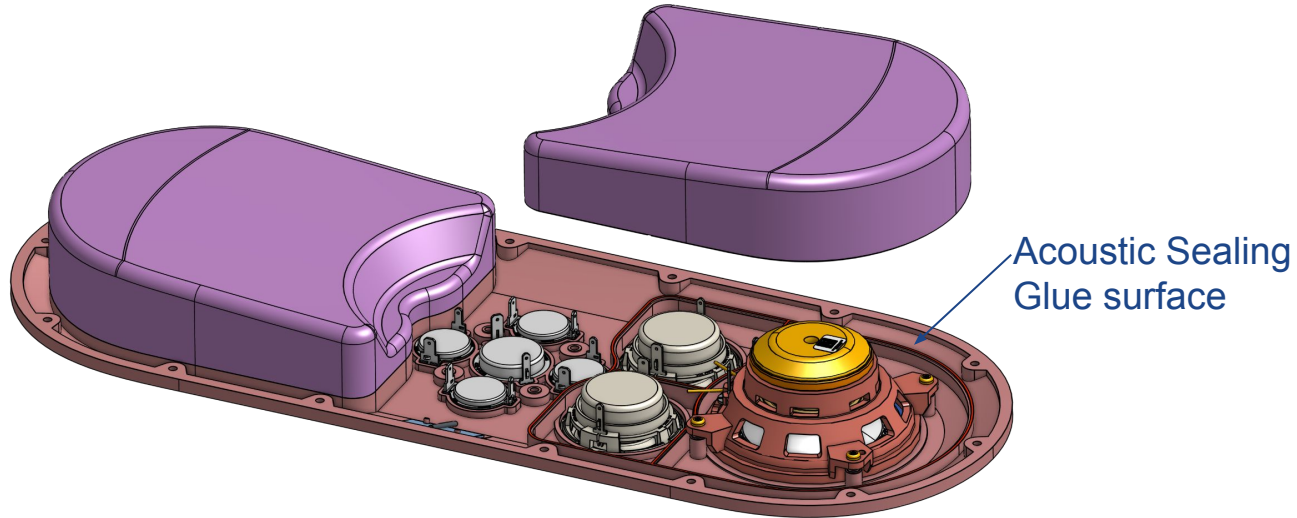

AE Challenge - Multi Element Array

Stereo Imaging, beam steering

Thermal challenge

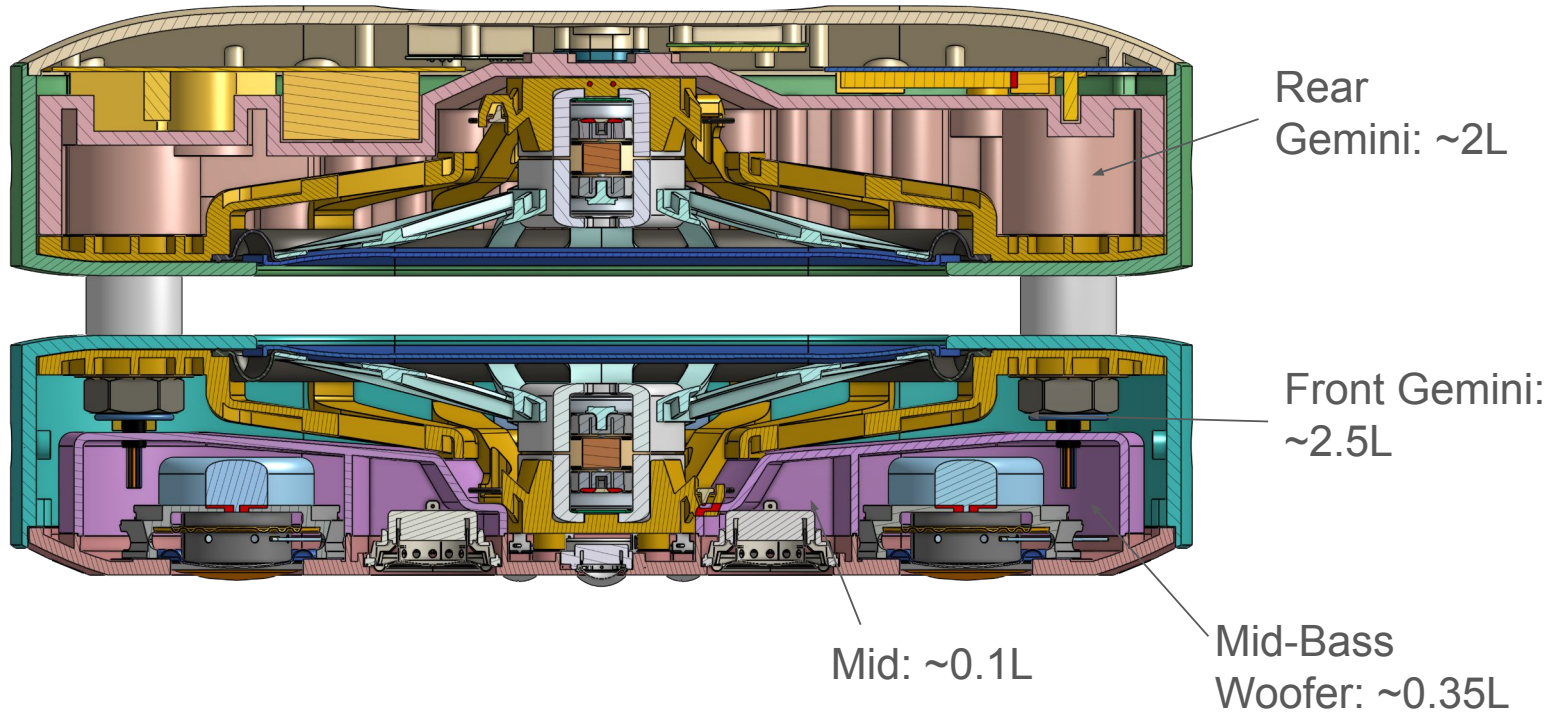

ME Challenge - Foot

Multiple Orientations

Hoagie -> Attached Base for Vertical, Integrated Feet for Horizontal

Design for Positional Stability walking and tip test. Base in Vertical, integrated feet in Horizontal. Being >7kgs means the following:

- *ME21 Test #3 and #5 become a requirement*
- *MS2 class for 62368-1 safety compliance testing of Relocation and Static Stability*
- *Note: Base height, and mass need to be studied for the impact to the vertical test*

Mounts and Stands

- *Floors stands are P0*
- *Wall Mounts are removed from PRD*

Check ME21 table tilt degree

VS updated IEC 60950-1

(IEC 62368-1 safety standard)



ME Challenge - Foot

Multiple Orientations

ME21 test #3 Static Tilt test table equipment


- *Tilt the tabletop 11 degrees from horizontal*
- *With the 11 degree tilt locked into position, rotate tabletop 360 degrees about its normal axis slowly ($1 \text{ rpm} \pm 0.2$)*
- *Glass surface*



ME Challenge - Pinch Hazard


2-enclosure with posts

- **Pinch Hazard:** *Finger Pinch Gaps between 5mm and 12mm are generally the "danger zone."*
- **Beta test:** https://docs.google.com/spreadsheets/d/1jfG6sEyTkcZsPWzq12Y2Rn907_PjF9yLbWPXFdnC97w/edit?gid=0#gid=0

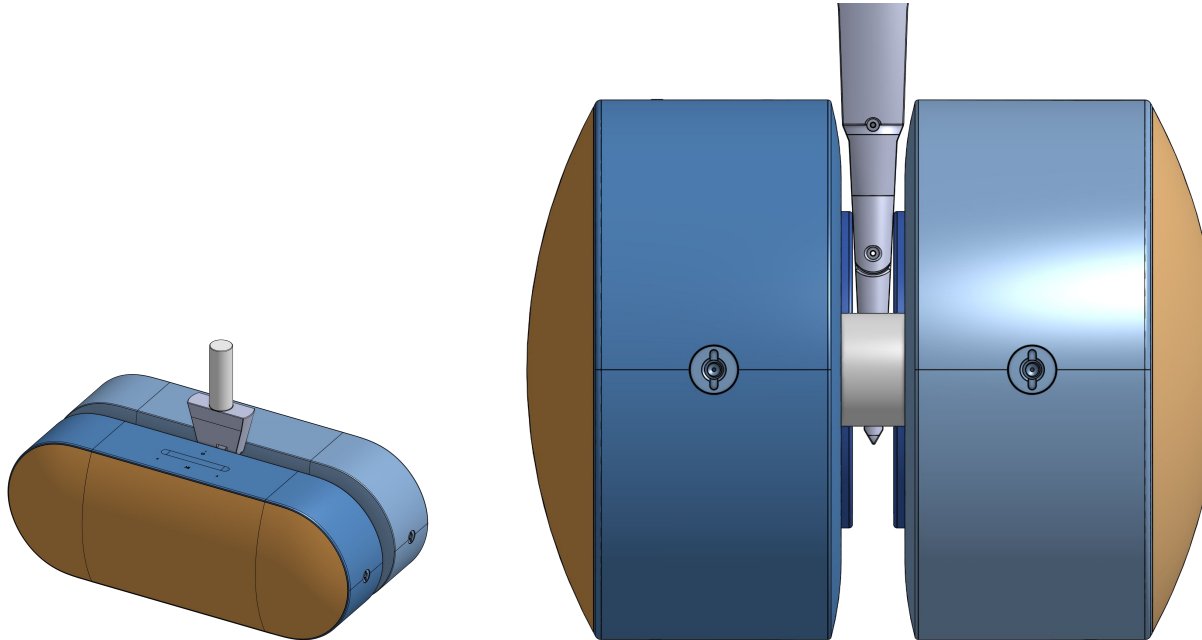

ME Challenge - High complexity & Small space


2-enclosure with posts

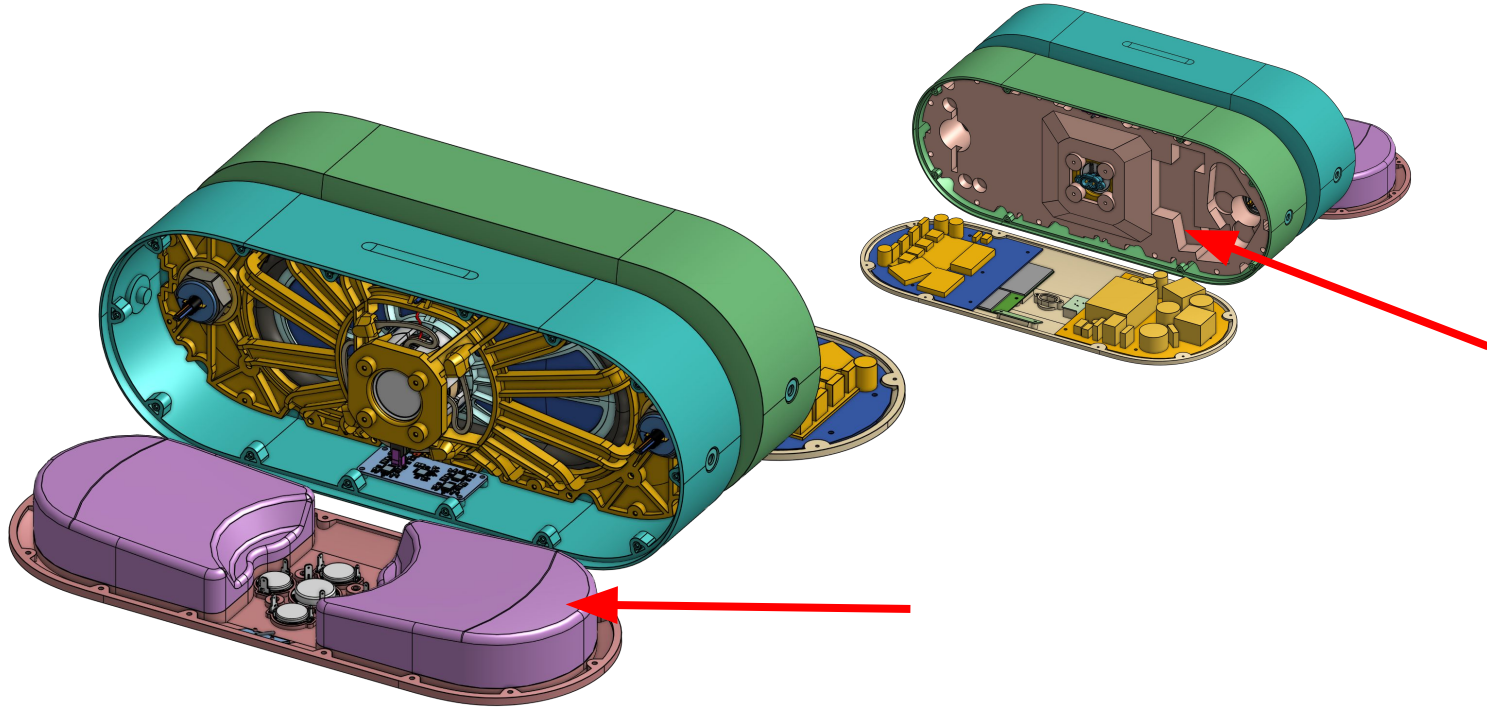

ME Challenge - High complexity & Small space

2-enclosure with posts

Where are we now?

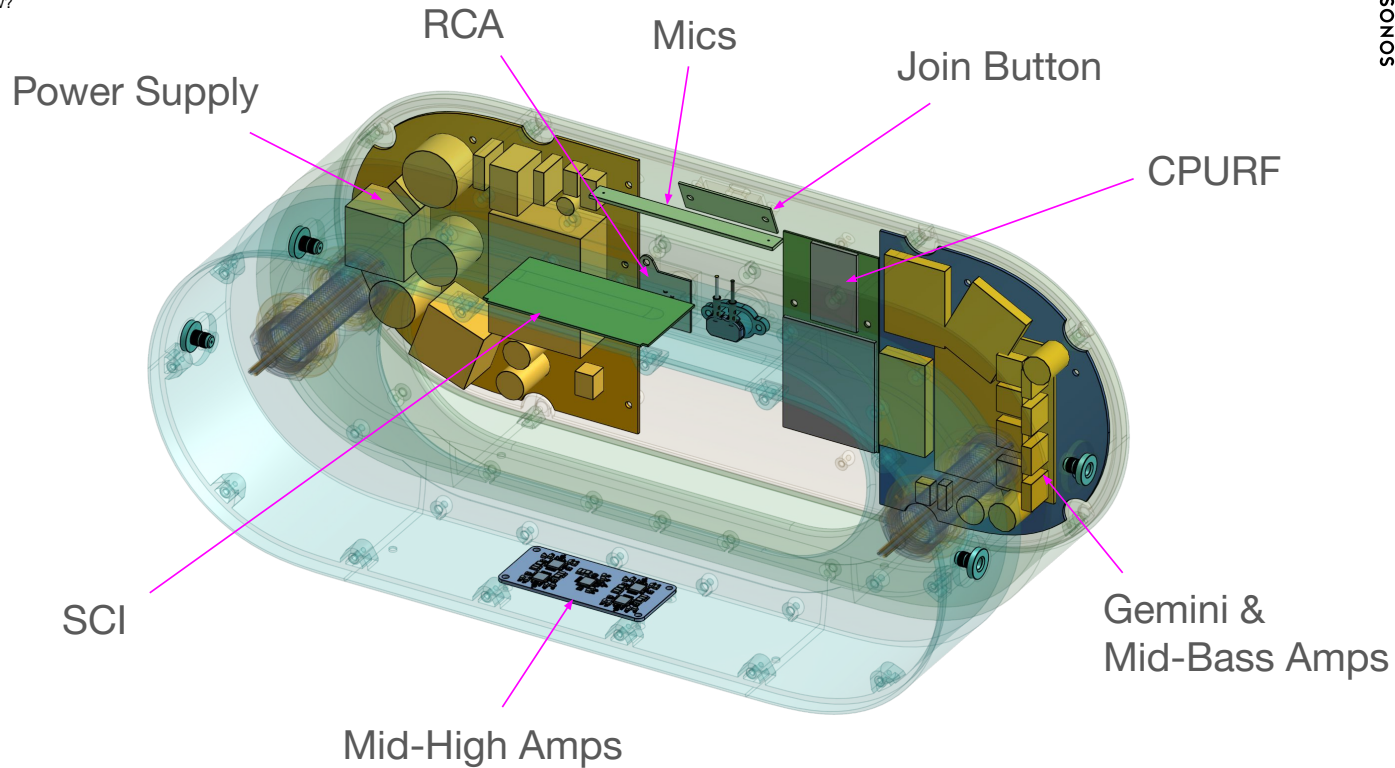

ME Challenge - High complexity & Small space

2-enclosure with posts



CPU-RF can fit in front or rear enclosure

Array amps go in front enclosure for best cost and fit

Preference for lowest EMI/EMC risk is to route all front-rear power and signal connections through a single post



Front Enclosure
CPU-RF + Array Amps

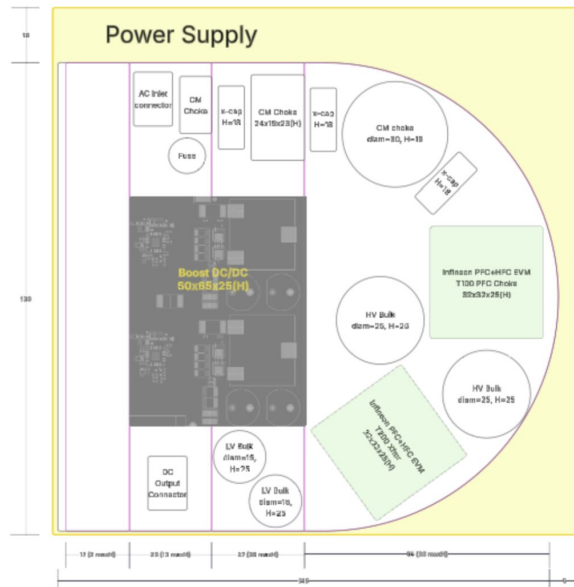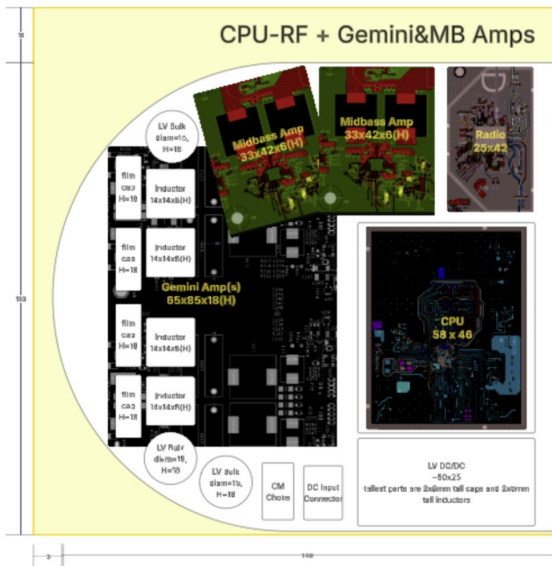


ME Challenge - Post Signaling

2-enclosure with posts

Split between posts - what's best for mitigation desense? EMI?


Single Post - how do we shield?

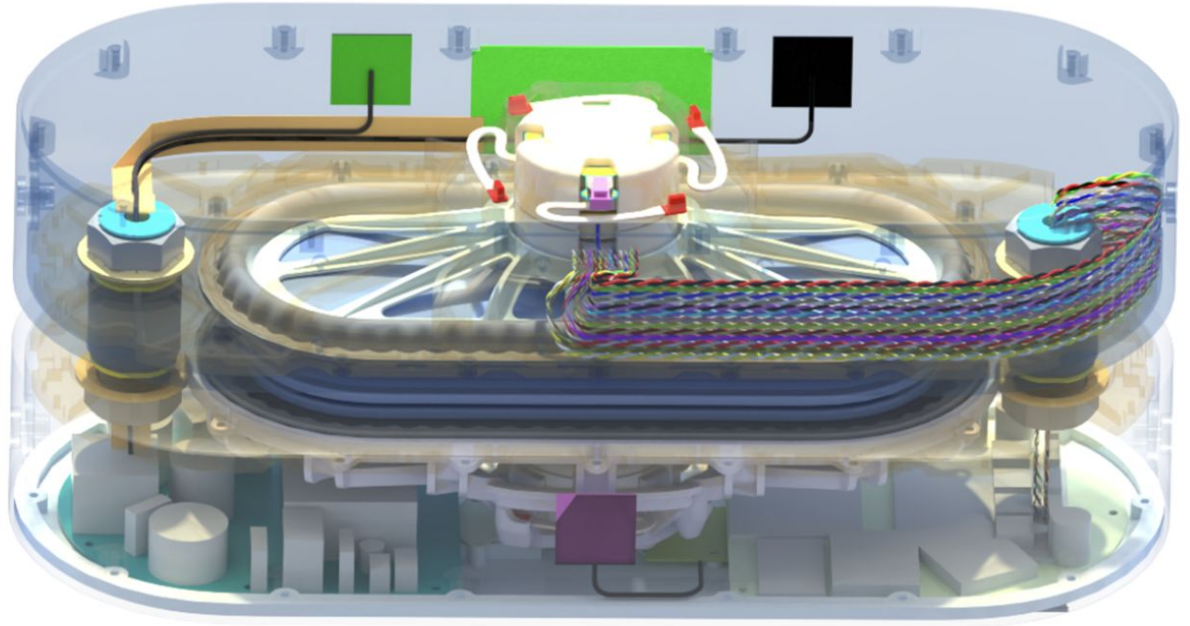

ME Challenge - PCBA thermal


2-enclosure with posts

How to attach thermocouple?

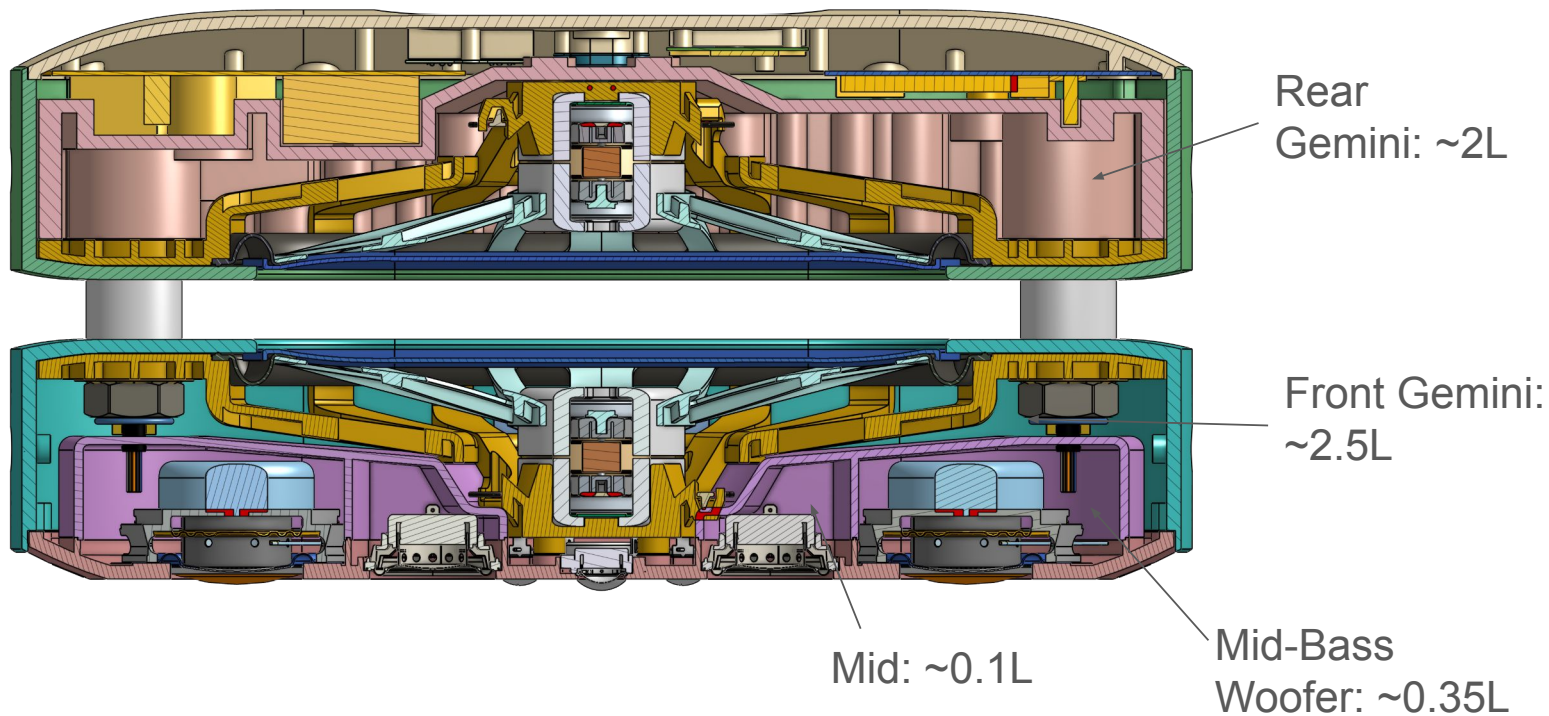

EE Challenge - More Power VS Less Space

System interconnection

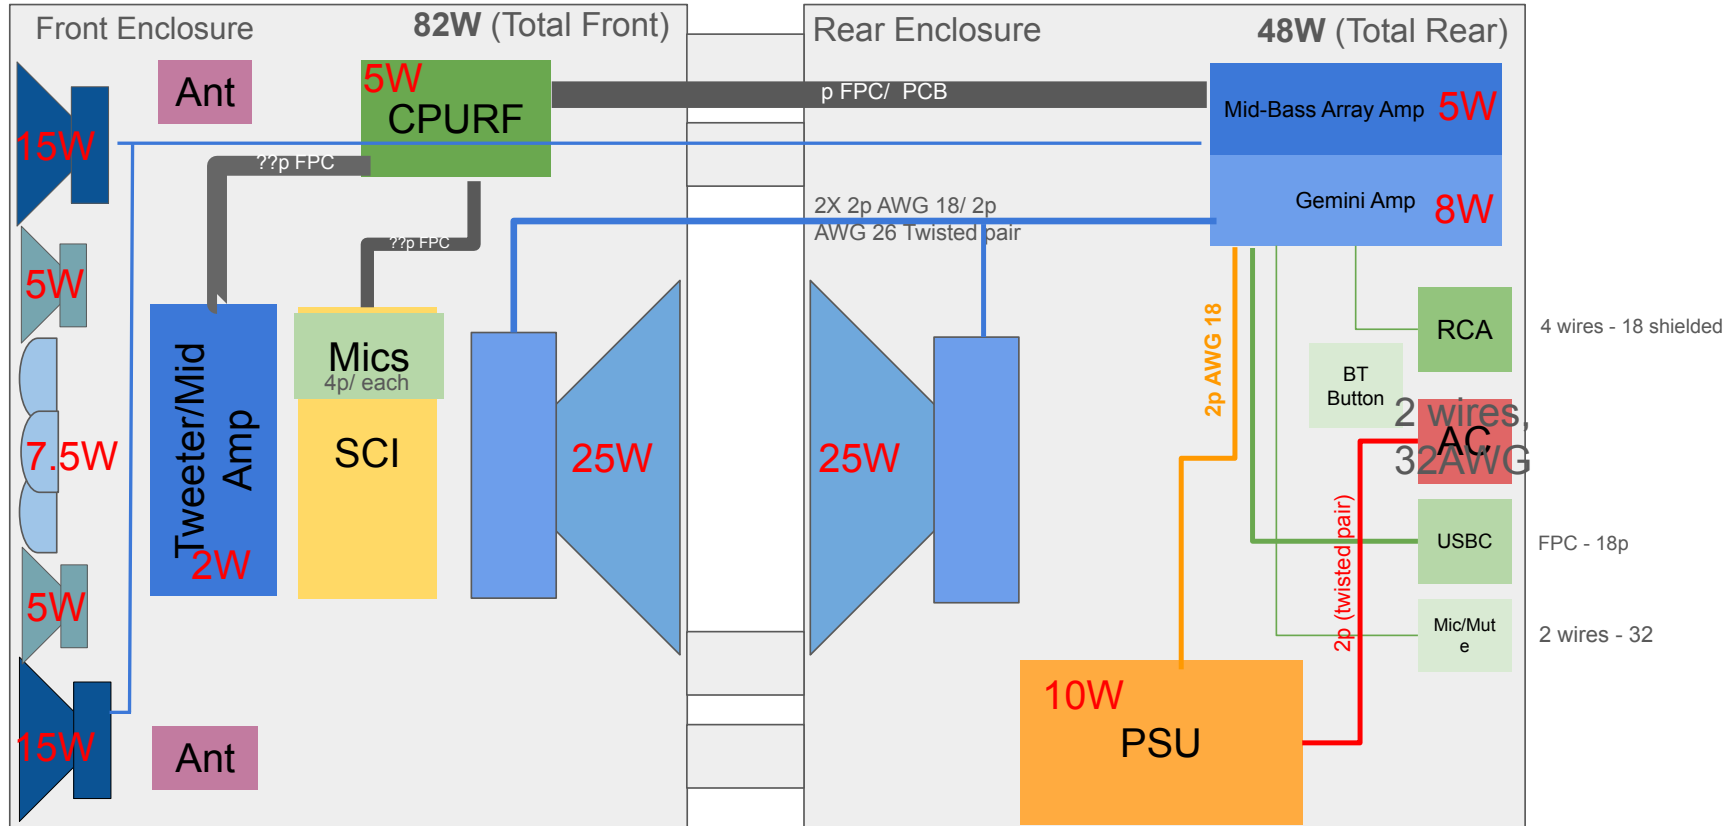

EE Challenge - Thermal Backoff

2 enclosure & 7 sealed cavity

If CPU/RF board, WFR/MID AMP board, PS board are all in back enclosure, how to detect front enclosure inner temperature?

- *NTC on array amp board?*
- *NTC on SCI board?*

How to tune DSP thermal backoff gain?

- *Integrated or Distributed ?*
- *Need to verify current algorithm fit 2 enclosure design*
- *For example, If CPU/RF board, WFR/MID AMP board, PS board are all in back enclosure which has extreme high temperature but front enclosure has normal temperature. Tune backoff-gain together? Or lower back enclosure Gemini only to keep performance for the best*

EE Challenge - Idle Power VS TTM

EU Standby Regulation requires < 2W

Options

1. Keep Everything On
Woofer Idling: ~0.75W/Woofer
X2 in Wireless Standby: 1.61W
Total Power est: **3.11W**

Liftoff Time: 0s
SoC Resume: <1s
TTM: Fastest option <1s

Change woofer to fit
power budget: 0.4W
budget, 75% PS Eff =
0.3W Woofer Budget

1a. Keep Everything On
Wfer Idling Req: **0.15W/Woofer**
X2 in Wireless Standby: 1.61W
Total Power est: **2W**

Liftoff Time: 0s
SoC Resume: <1s
TTM: Fastest option <1s
Note: not feasible

Sonos Confidential

2. Land Gemini
Woofer: 0W
X2 in Wireless Standby: 1.61W
Total Power est: 1.61W

Liftoff Time: 1-2s/woofer
SoC Resume: <1s
TTM: **2-4s**

*Note: faster time is
simultaneous liftoff which is 2x
the power*

Reduce Liftoff
Time

2a. Land Gemini
Woofer: 0W
X2 in Wireless Standby: 1.61W
Total Power est: 1.61W

Liftoff Time: <1s
SoC Resume: <1s
TTM: <1s
*Note: Requires 1.2kW or
reduction in Neg K*

3. Idle Gemini SoC Suspend
Woofer Idling: ~0.75W/Woofer
X2 in Suspend: 0.79W
Total Power est: **<2.29W**

Liftoff Time: 0s
SoC Resume: 1-2s
TTM: 1-2s

*Note: need SW support of SoC
Suspend (not productized yet)*

Loading Earcon

2b. Land Gemini
Woofer: 0W
X2 in Wireless Standby: 1.61W
Total Power est: 1.61W

Liftoff Time: 1-2s/woofer
SoC Resume: <1s
TTM: **2-4s**
*Note: Use array earcon to
reduce perceptual TTM*

4. Land Gemini SoC Suspend
Woofer: 0W
X2 in Suspend: <1W
Total Power est: <1W

Liftoff Time: 1-2s/woofer
SoC Resume: 1-2s
TTM: 2-4s

*Note: you're doing too much
work and saving extra power!*

Longer TTM

Recommended

2c. Land Gemini
Woofer: 0W
X2 in Wireless Standby: 1.61W
Total Power est: 1.61W

Liftoff Time: 1-2s/woofer
SoC Resume: <1s
TTM: 2-4s
*Note: Proactively launch
Gemini to reduce long TTM
possibilities*

SONOS

Delay

2d.
Wc
X2
Tot

Lift
So
TT

No
wo
pre

EE Challenge - Idle Power VS TTM

SOC idle power + Gemini power

We do not plan to use sleep to get to 2W. We plan to "land" Gemini and turn off the amps. We know this will in turn come at the cost of increased TTM from the idle state because you need to wait for booth woofers to lift off in order to play audio again. We still need to define a TTM spec but this compromise is better than other options.

- *SOC semi-standby not suspend about 1.6W*

Let's say for technical reasons that we simply can't achieve <2W network standby on Olympia even with the woofers landed, but we can achieve it in sleep (SoC suspend) state.


- *This is the reason why we still need to test LPS for Olympia*

HWV how to test idle power and TTM? - GGEC


EE Challenge - Idle Power VS TTM

Gemini power off & Liftoff

In-to-Out

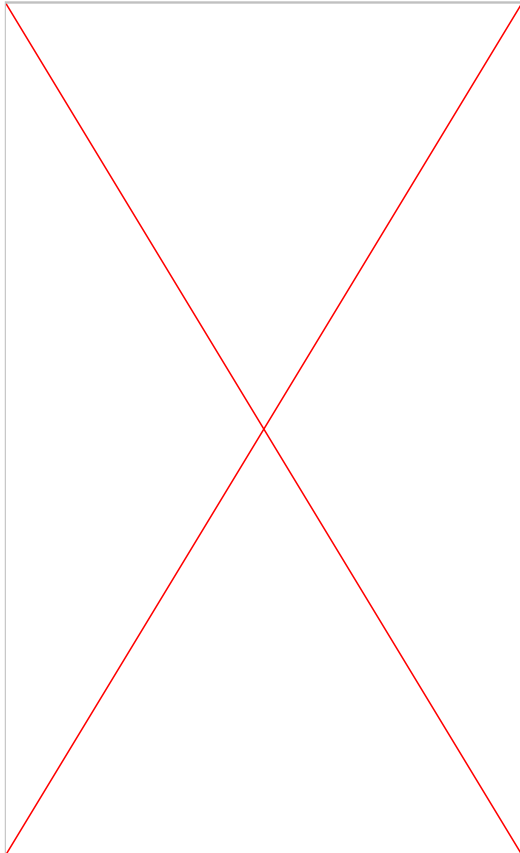


Out-to-In

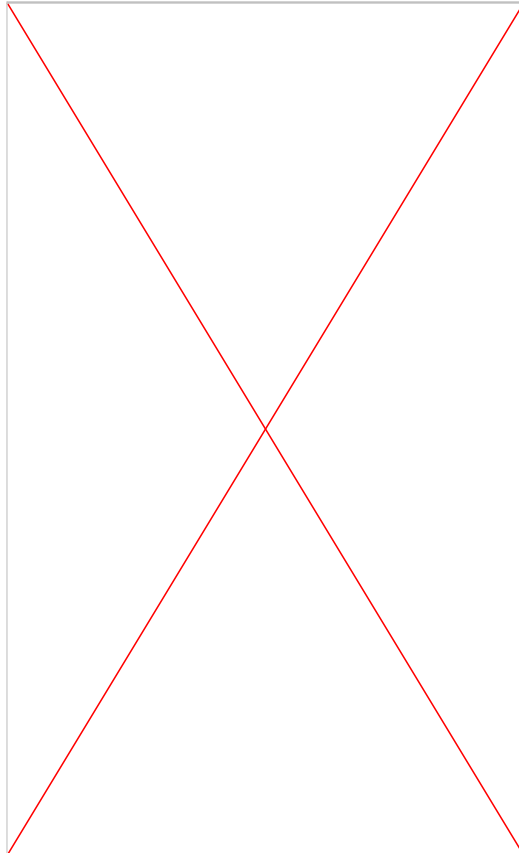


EE Challenge - Idle Power VS TTM

Gemini power off & Liftoff


Small Sealed box +
Gemini

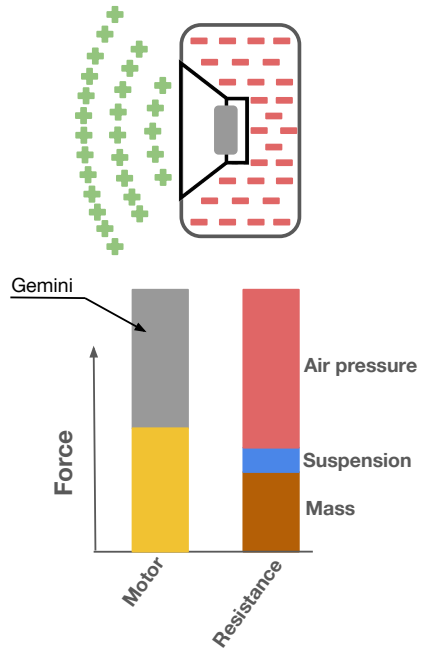

Small Sealed box +
Gemini **Power off**

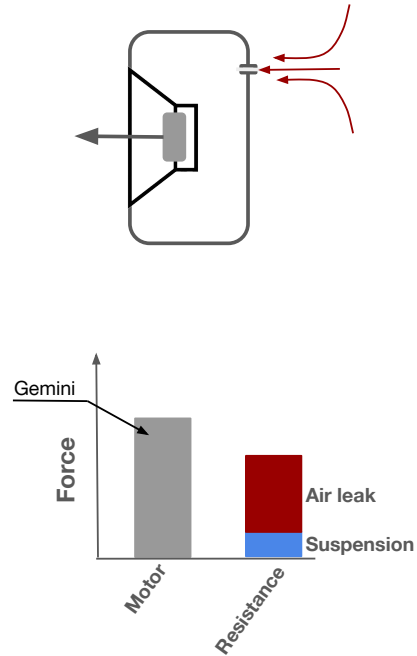



Small Sealed box +
Gemini **Power off**

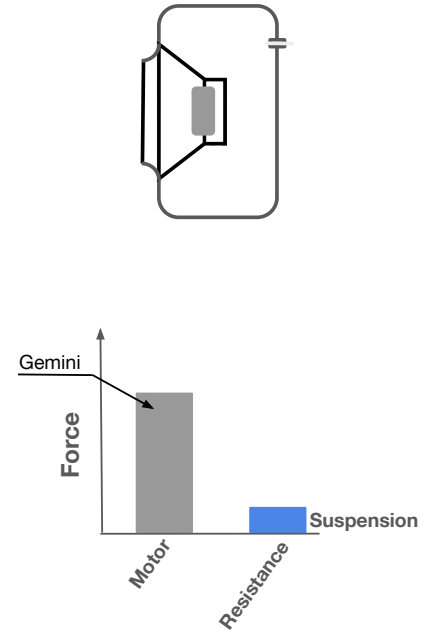



EE Challenge - Idle Power VS TTM

Gemini power off & Liftoff

Small Sealed box +
Gemini **Power off**

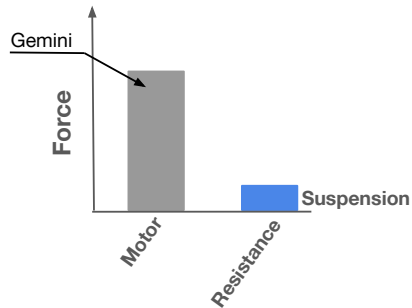



Small Sealed box +
Gemini **Lift off**

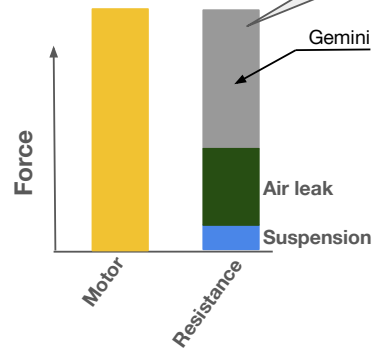

Gemini is **assistive**
during music playback,
but **resistive** at lift off

Small Sealed box +
Gemini with Music

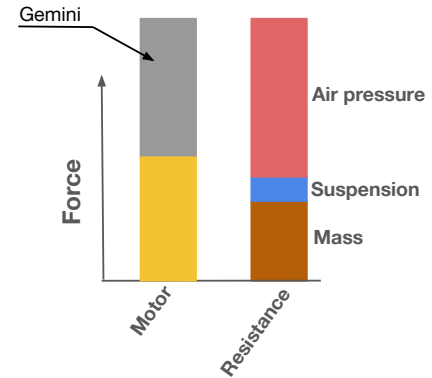

EE Challenge - USB Line-in & RCA

HWV tests

How to test USB line-in? - GGEC

- *RPT?*
- *ENV operating?*
- *ADMT?*
- *EDMT?*

How to test RCA? - GGEC

- *RPT?*
- *Audio DVT?*
- *ADMT?*
- *EDMT?*

How to test HiFi?

EE Challenge - EMC Risks

Compliance

Olympia is at high risk for radiated/conducted emission due to:

- *High power in tight spaces (electronics/wiring/PCBA's close together with a high power output)*
- *Close bundling of wires through tight spaces*
- *New DC amplifier design*

This will require early and frequent EMI testing (RE/CE), troubleshooting, and improvements over each prototype phase.

Multiple orientations for EMI testing?

GGEC how to do pre-test in early stage? Third-party or in-house testing?

Project Schedule

P1/P2A/P2B/EVT/DVT and PVT

Creation Phase	Date	Status	Notes
SRR		GREY	
ACR	14 Apr 2026	GREEN	
ADR	01 Jun 2026	GREEN	
SDR		GREY	
P1A Build	20 Jul 2026	GREY	3D Printed Proto System Build
CP1	14 Aug 2026	GREY	
Prototype Commit	17 Aug 2026	GREY	

Project Schedule

P1/P2A/P2B/EVT/DVT and PVT

Prototyping Phase	Date	Status	Notes
PDR		GREY	
P1B Build	14 Sep 2026	GREY	Rapid Proto build, catch adjustments before tooling release
P2A Build	23 Nov 2026	GREY	Material Intent Assembly
Pre-Build DR		GREY	
P2B Build	01 Mar 2027	GREY	
CDR		GREY	
CP2	23 Apr 2027	GREY	

Project Schedule

P1/P2A/P2B/EVT/DVT and PVT

Realization Phase	Date	Status	Notes
EVT Build	14 Jun 2027	GREY	
TAR		GREY	
DVT Build	06 Sep 2027	GREY	
PRR		GREY	
CP3	08 Oct 2027	GREY	

Project Schedule

P1/P2A/P2B/EVT/DVT and PVT

Launch Phase	Date	Status	Notes
PVT Build	15 Nov 2027	GREY	
MPR		GREY	
MP	29 Nov 2027	GREY	
GA Ready	21 Feb 2028	GREY	14weeks from PVT LT slowboat

P1A Test Plan

Timing · PCBA configurations · HWV thermal strategy

Index	Focus	Procedure	Priority	Should/Shall	Tester	Config Needed
Thermal	1. Hardware thermal design (ME/EE) 2. Transducer & Gemini demagnetization temperatures 3. Thermal simulation calibration	Thermal test plan Sonos provide	High	Should	JDM	Config A
Boot	1. SoC boot up 2. Hardware drivers installation	Boot test plan Sonos provide	High	Should	JDM	OF
LPS	1. Standby power check 2. SoC suspend function check	LPS test plan Sonos provide	Low	Shall	JDM	OF
ME21	Removable Feet – Multi Orientation	ME21 PFS	Medium	Should	JDM	Config A
Audio_DVT	New AMPs with Low distortion	Audio_DVT plan	Low	Shall	JDM	OF

Verification Scope & Criteria

The what and where of HWV testing for Olympia



Part 1 · PKG · ME · ENV · CMF



Part 2 · EE · DMT · Group D · Other

Verification Scope & Criteria (1/2)

Packaging · Mechanical · Environment · CMF



Packaging

- PKG4-1 High temp storage
- PKG4-2 High temp + humidity
- PKG5 Low temp storage
- PKG10 ISTA-3A



Mechanical

- ME2 Product drop
- ME19 Cord Integrity
- ME20 I/O Jack Durability
- ME21 Position stability
- ME24 Button Travel
- ME29 Foot staining
- ME30 Foot durability
- ME37 Tilt Drop
- ME39 Button Tactility Durability



Environment

- ENV1 High temp operational
- ENV2 Low temp operational
- ENV3 Temp cycling
- ENV4 High temp + humidity
- ENV5 Unpkg. high temp storage
- ENV6 Unpkg. low temp storage
- ENV7 Unpkg. thermal shock
- ENV8 Salt Mist Cyclic
- ENV11 Env. stress cracking



CMF

- CMF1 Scratch resistance
- CMF2 Abrasion resistance
- CMF3 Chemical resistance
- CMF4 Paint adhesion
- CMF5 UV stability
- CMF6 Wipe ability

Verification Scope & Criteria (2/2)

Electronics · Design Maturity Test · Special EE · Other



Electronics

- Thermal
- Audio DVT
- Boot test
- PS DVT
- LPS
- CPU SI



DMT

- ADMT (1000 hrs)
- EDMT (19 + 19 days)
- TBD



Special EE

- US3 Physical Mic On/Off Switch Cycle
- Signature detail (Ghost touch)
- CPU crystal spurs
- PS Abnormal



Other

- EVN12 Altitude test
- GGEC to propose ?

Documentations

Where everything lives for Olympia HWV

Documentation · Where to find everything

Joint Development Resources:

- *#ext-ggrec-olympia-pd Slack*
- *#ext-sonos-ggrec-olympia-hwv Slack*
- *Ext Olympia GGEC Confluence Space*
- *GGEC > Olympia Box Folder*

Thanks!
